

Start Date: 02JUL07
 Finish Date: 11FEB17
 Data Date: 01AUG07

© Primavera Systems, Inc.

Legend:
 Early Bar: Green
 Progress Bar: Blue
 Critical Activity: Red

Sheet 1 of 1

Malibu HS


Draft Preliminary Schedule

Date	Revision	Checked	Approved


Orig Dur	Early Start	Early Finish	2007												2008												2009												2010											
			J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J

Malibu HS		
Measure BB		
Pkg #2 (HVAC - Locker Rooms)		
Preconstruction		
HVAC Locker Rooms		
180 01JAN08	28JUN08	
60 29JUN08	27AUG08	
60 29JUN08	27AUG08	
120 28AUG08	25DEC08	
60 26DEC08	23FEB09	

Construction		
HVAC Locker Rooms		
180 24FEB09	22AUG09	
Close-Out		
HVAC Locker Rooms		
90 23AUG09	20NOV09	

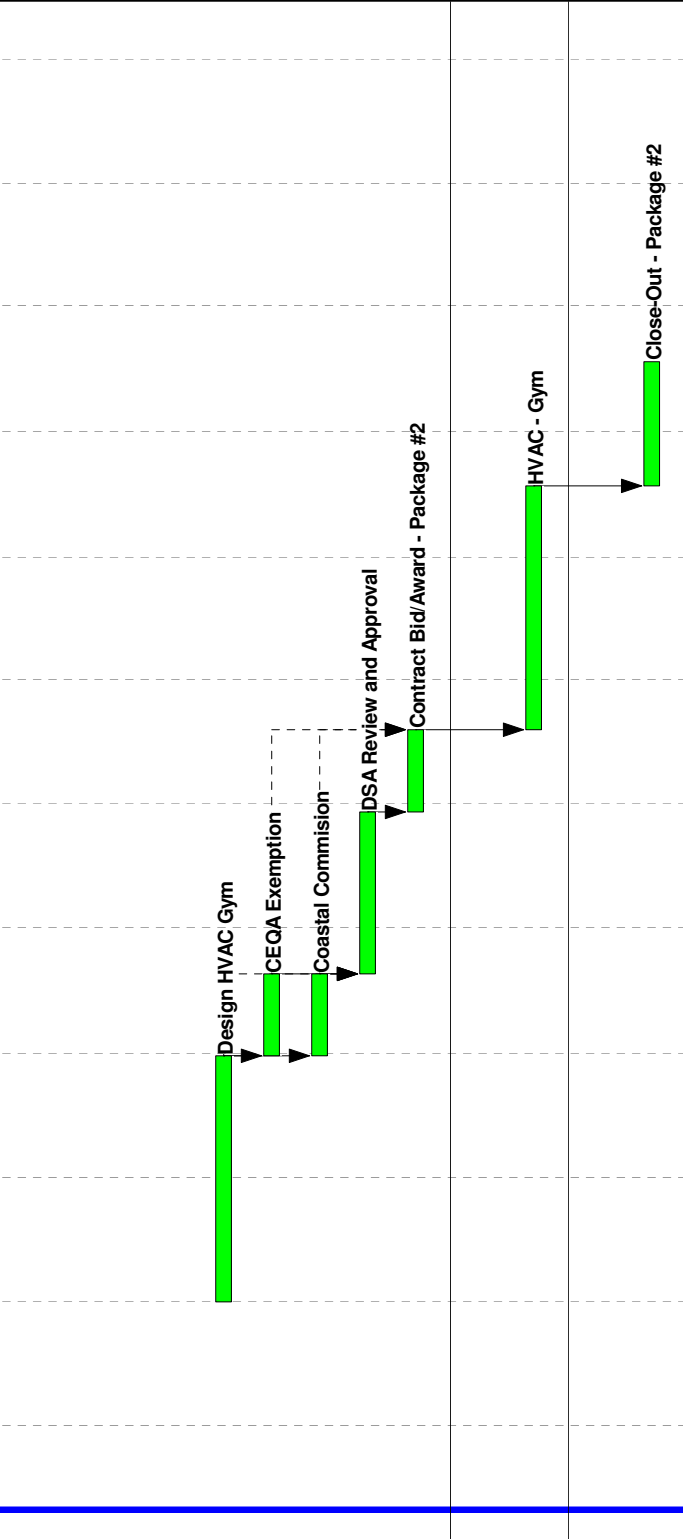

Start Date	02JUL07	MAST		Sheet 1 of 1
Finish Date	11FEB17			
Data Date	01AUG07			
Run Date	22AUG07 16:35			
© Primavera Systems, Inc.				
		Malibu HS Draft Preliminary Schedule		
		Date	Revision	Checked
				Approved

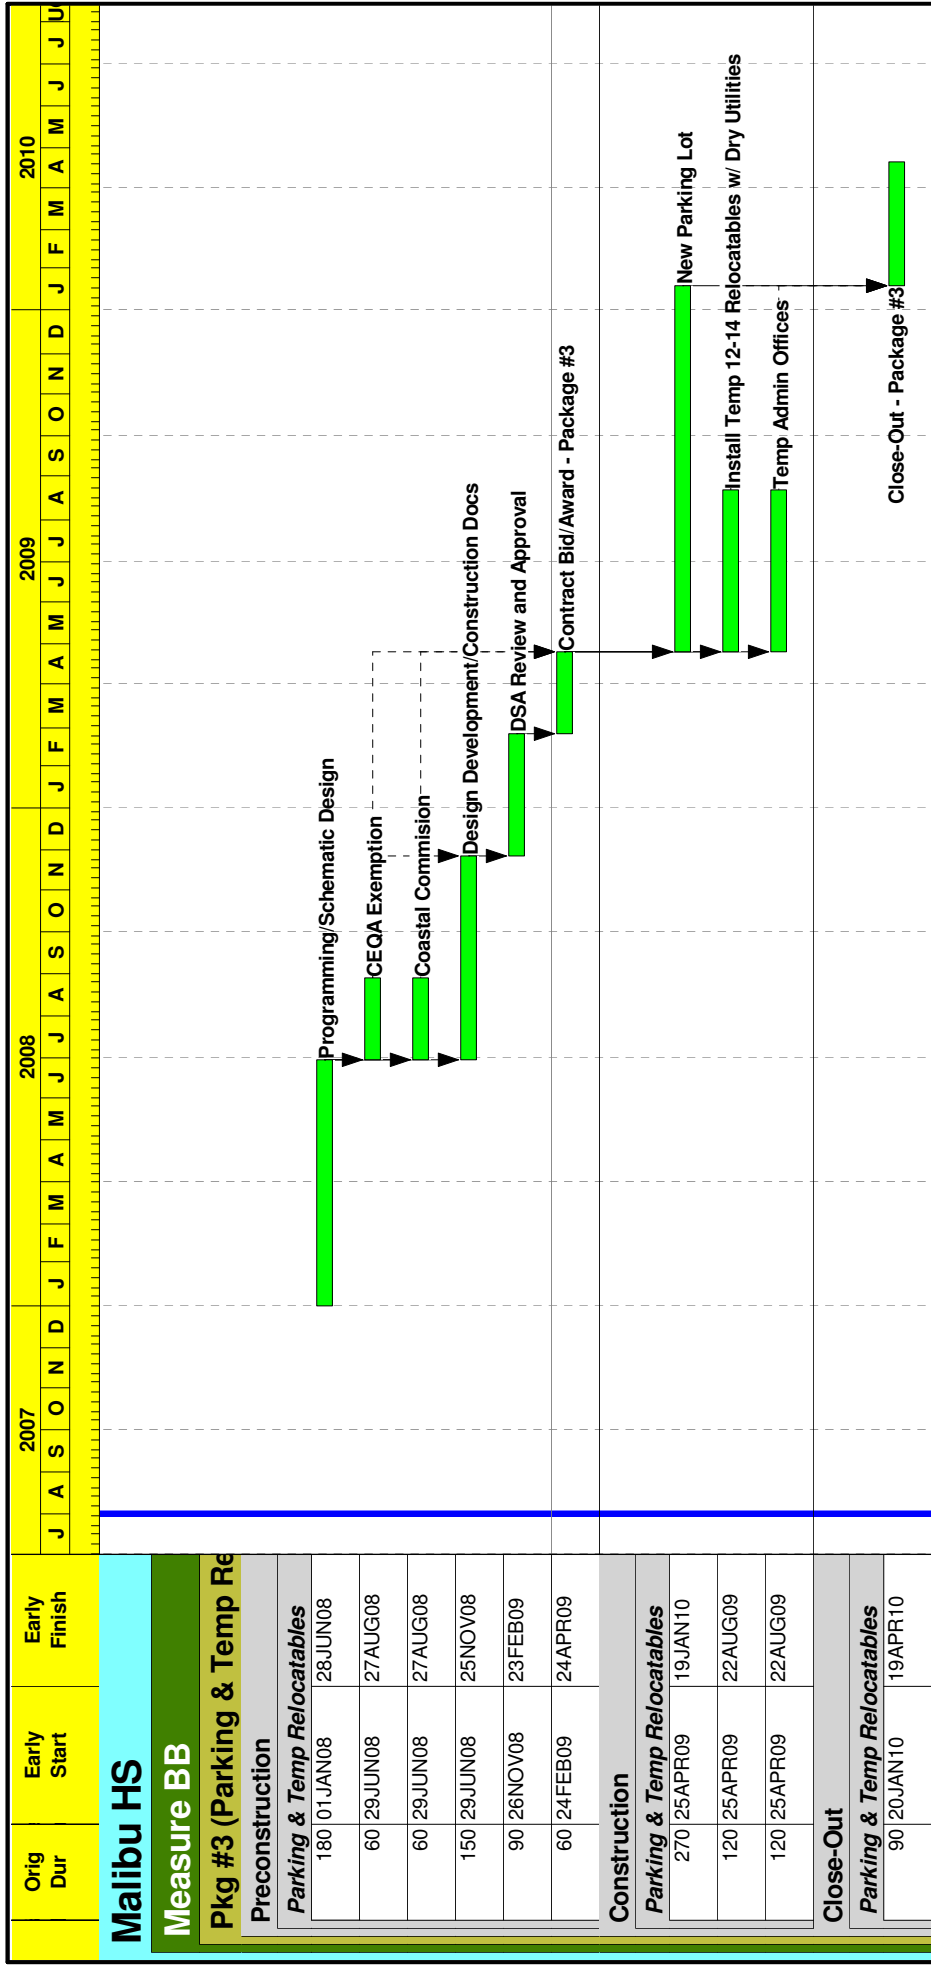

Sheet 1 of 1


MAST

- █ Early Bar
- █ Progress Bar
- █ Critical Activity

Start Date	02JUL07
Finish Date	11FEB17
Data Date	01AUG07
Run Date	22AUG07 16:35

Malibu HS Draft Preliminary Schedule

Date	Revision	Checked	Approved

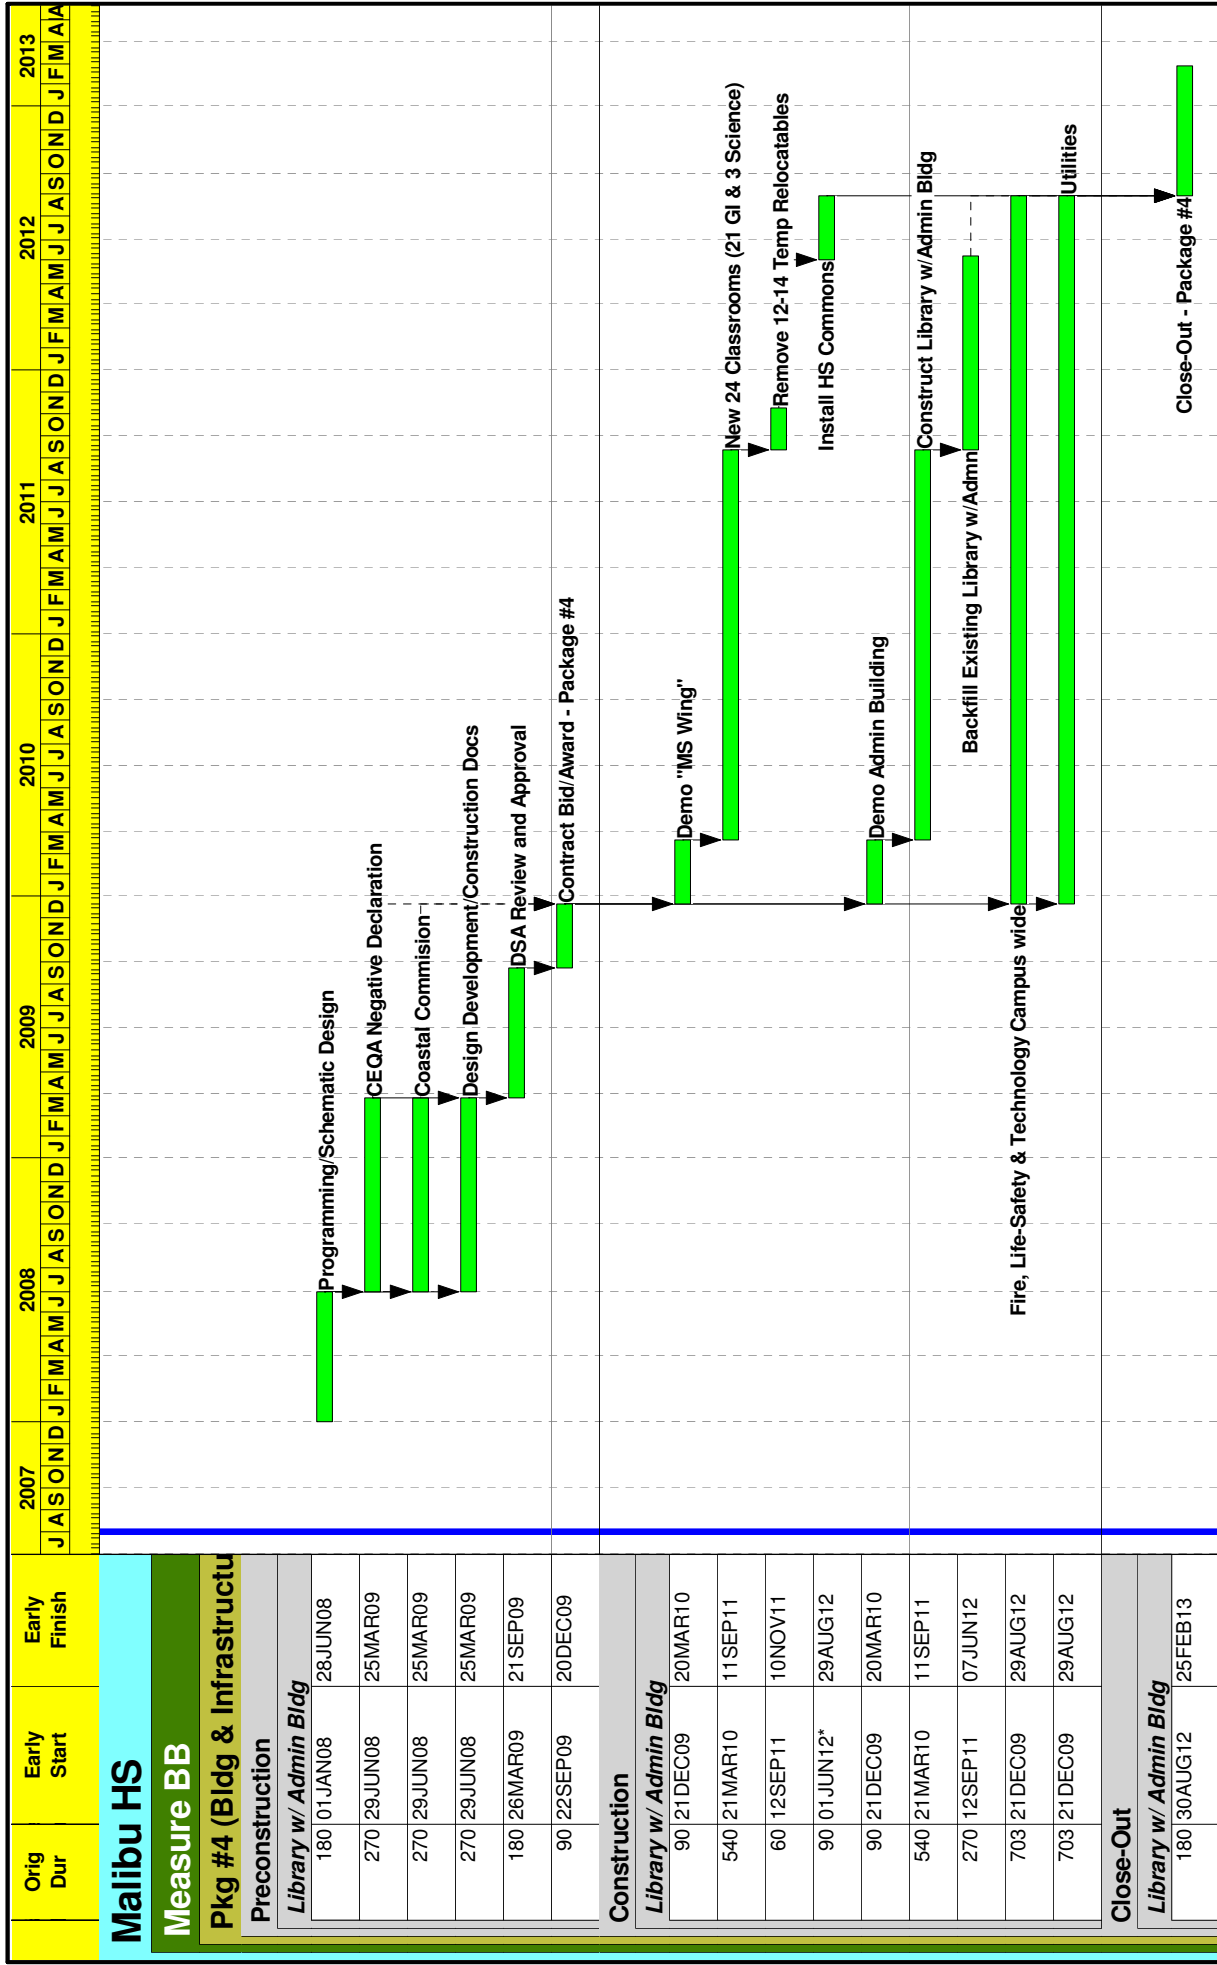

Start Date: 02JUL07
 Finish Date: 11FEB17
 Data Date: 01AUG07
 Run Date: 22AUG07 16:33

Legend:
█ Early Bar
█ Progress Bar
█ Critical Activity


© Primavera Systems, Inc.

Sheet 1 of 1

Malibu HS

Draft Preliminary Schedule

Date	Revision	Checked	Approved

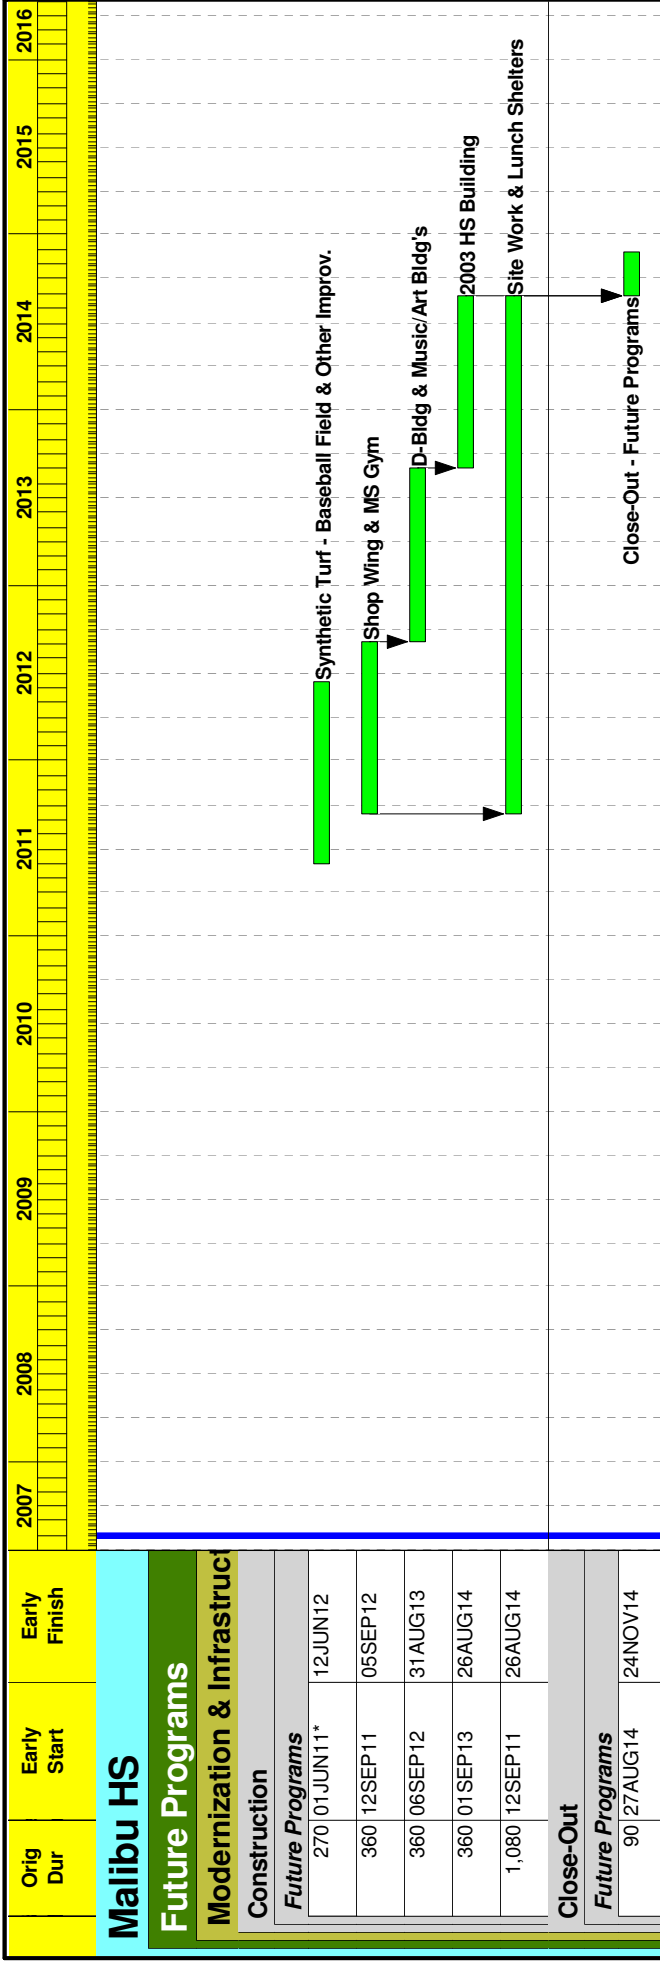

Start Date	02 JUL 07	MAST	Sheet 1 of 1
Finish Date	11 FEB 17		
Data Date	01 AUG 07		
Run Date	22 AUG 07 16:34		
Malibu HS Draft Preliminary Schedule			
<div style="display: flex; justify-content: space-around;"> <div style="text-align: center;"> █ Early Bar </div> <div style="text-align: center;"> █ Progress Bar </div> <div style="text-align: center;"> █ Critical Activity </div> </div>			
Date	Revision	Checked	Approved
© Primavera Systems, Inc.			

Activity ID	Activity Description	Orig Dur	Early Start	Early Finish	Budgeted Cost in Million	2008	2009	2010	2011	2012	2013	2014	2015	2016	2017	2018	2019

Malibu HS

Measure BB

Pkg #1 (Athletic Facilities)

Preconstruction

Athletic Facilities

MHS2110	Design Synthetic Turf & Tennis Court	60	01JAN08	29FEB08	0.00
MHS2120	DSA Review and Approval	60	01MAR08	29APR08	0.00
MHS2130	CEQA Exemption	60	01MAR08	29APR08	0.00
MHS2140	Coastal Commission	60	01MAR08	29APR08	0.00
MHS4130	Bid/Award - Package #1	60	30APR08	28JUN08	0.00

Construction

Athletic Facilities

MHS5090	Synthetic Turf	180	29JUN08	25DEC08	30.91
MHS5100	Tennis Courts	120	29JUN08	26OCT08	0.00

Close-Out

Athletic Facilities

MHS6100	Close-Out - Package #1	60	26DEC08	23FEB09	0.30
---------	------------------------	----	---------	---------	------

Pkg #2 (HVAC - Locker Rooms Competition Gym)

Preconstruction

HVAC Locker Rooms

MHS2030	Design HVAC Gym	180	01JAN08	28JUN08	0.91
MHS2040	CEQA Exemption	60	29JUN08	27AUG08	0.00
MHS2050	Coastal Commission	60	29JUN08	27AUG08	0.00
MHS2070	DSA Review and Approval	120	28AUG08	25DEC08	0.30
MHS4080	Contract Bid/Award - Package #2	60	26DEC08	23FEB09	0.06

Construction

HVAC Locker Rooms

MHS5130	HVAC - Gym	180	24FEB09	22AUG09	0.00
---------	------------	-----	---------	---------	------

Close-Out

HVAC Locker Rooms

MHS6140	Close-Out - Package #2	90	23AUG09	20NOV09	0.00
---------	------------------------	----	---------	---------	------

Pkg #3 (Parking & Temp Relocatables)

Preconstruction

Parking & Temp Relocatables

MHS2200	Programming/Schematic Design	180	01JAN08	28JUN08	0.91
MHS2210	CEQA Exemption	60	29JUN08	27AUG08	0.00
MHS2220	Coastal Commission	60	29JUN08	27AUG08	0.00
MHS2230	Design Development/Construction Docs	150	29JUN08	25NOV08	2.66
MHS2240	DSA Review and Approval	90	26NOV08	23FEB09	0.30
MHS4250	Contract Bid/Award - Package #3	60	24FEB09	24APR09	0.06

Construction

Parking & Temp Relocatables

MHS5260	New Parking Lot	270	25APR09	19JAN10	0.00
MHS5270	Install Temp 12-14 Relocatables w/ Dry Utilities Temporary	120	25APR09	22AUG09	0.00
MHS5280	Temp Admin Offices	120	25APR09	22AUG09	0.00

Close-Out

Parking & Temp Relocatables


MHS6290	Close-Out - Package #3	90	20JAN10	19APR10	0.00
---------	------------------------	----	---------	---------	------

Pkg #4 (Bldg & Infrastructure)

Preconstruction

Library w/ Admin Bldg

MHS2300	Programming/Schematic Design	180	01JAN08	28JUN08	0.91
---------	------------------------------	-----	---------	---------	------

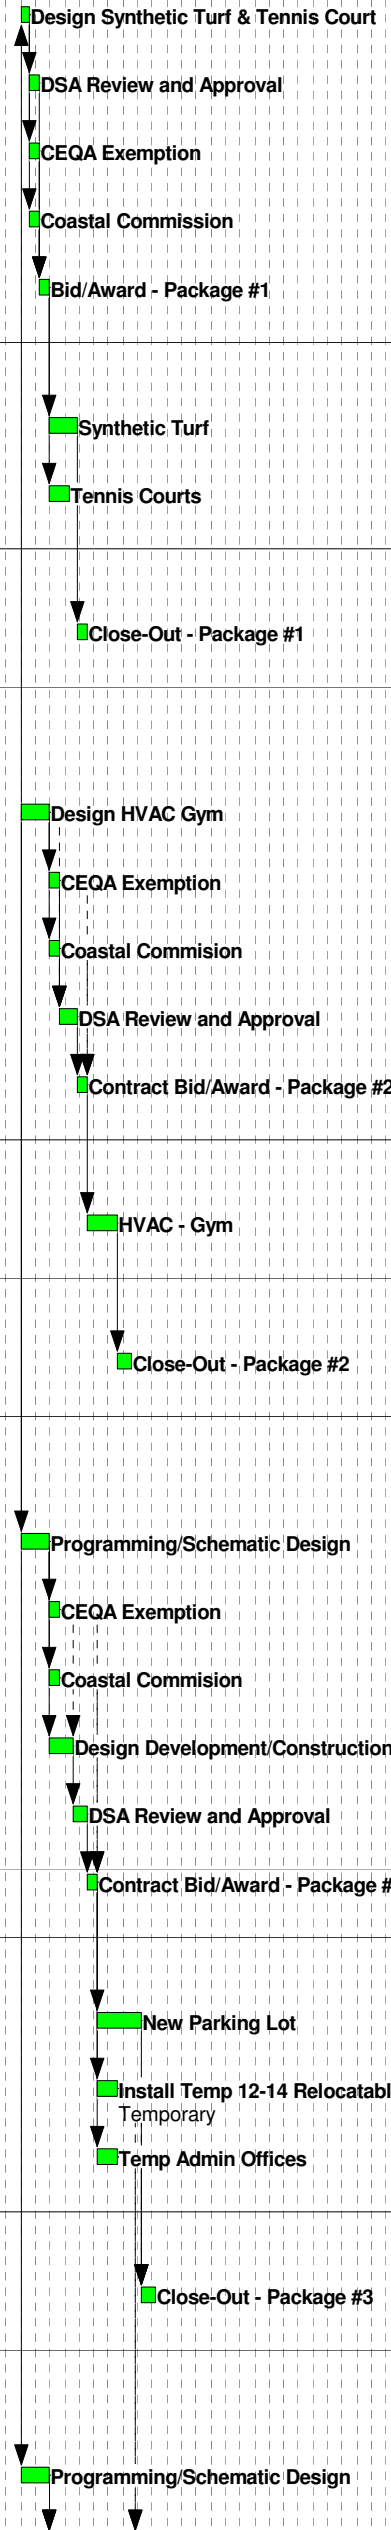

Start Date	02JUL07		Early Bar
Finish Date	11FEB17		Progress Bar
Data Date	01AUG07		Critical Activity
Run Date	22AUG07 13:39		

MAST

Sheet 1 of 2

Malibu HS Draft Preliminary Schedule

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Early Start	Early Finish	Budgeted Cost in Million	2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018 2019											
						Gantt Chart											
MHS2310	CEQA Negative Declaration	270	29JUN08	25MAR09	0.00	[Gantt Bar]											
MHS2320	Coastal Commision	270	29JUN08	25MAR09	0.00	[Gantt Bar]											
MHS2330	Design Development/Construction Docs	270	29JUN08	25MAR09	2.66	[Gantt Bar]											
MHS2340	DSA Review and Approval	180	26MAR09	21SEP09	0.30	[Gantt Bar]											
MHS4350	Contract Bid/Award - Package #4	90	22SEP09	20DEC09	0.06	[Gantt Bar]											
Construction																	
Library w/ Admin Bldg																	
MHS5360	Demo "MS Wing"	90	21DEC09	20MAR10	0.00	[Gantt Bar]											
MHS5370	New 24 Classrooms (21 GI & 3 Science)	540	21MAR10	11SEP11	0.00	[Gantt Bar]											
MHS5380	Remove 12-14 Temp Relocatables	60	12SEP11	10NOV11	0.00	[Gantt Bar]											
MHS5390	Install HS Commons	90	01JUN12*	29AUG12	0.00	[Gantt Bar]											
MHS5400	Demo Admin Building	90	21DEC09	20MAR10	0.00	[Gantt Bar]											
MHS5410	Construct Library w/Admin Bldg	540	21MAR10	11SEP11	0.00	[Gantt Bar]											
MHS5420	Backfill Existing Library w/Admn	270	12SEP11	07JUN12	0.00	[Gantt Bar]											
MHS5430	Fire, Life-Safety & Technology Campus wide	703	21DEC09	29AUG12	0.00	[Gantt Bar]											
MHS5440	Utilities	703	21DEC09	29AUG12	0.00	[Gantt Bar]											
Close-Out																	
Library w/ Admin Bldg																	
MHS6300	Close-Out - Package #4	180	30AUG12	25FEB13	0.00	[Gantt Bar]											
Future Programs																	
Modernization & Infrastructure																	
Construction																	
Future Programs																	
MHS5305	Synthetic Turf - Baseball Field & Other Improv.	270	01JUN11*	12JUN12	0.00	[Gantt Bar]											
MHS5310	Shop Wing & MS Gym	360	12SEP11	05SEP12	0.00	[Gantt Bar]											
MHS5320	D-Bldg & Music/Art Bldg's	360	06SEP12	31AUG13	0.00	[Gantt Bar]											
MHS5330	2003 HS Building	360	01SEP13	26AUG14	0.00	[Gantt Bar]											
MHS5340	Site Work & Lunch Shelters	1,080	12SEP11	26AUG14	0.00	[Gantt Bar]											
Close-Out																	
Future Programs																	
MHS6350	Close-Out - Future Programs	90	27AUG14	24NOV14	0.00	[Gantt Bar]											

Start Date 02JUL07
 Finish Date 11FEB17
 Data Date 01AUG07
 Run Date 22AUG07 13:39

█ Early Bar
█ Progress Bar
█ Critical Activity

MAST Sheet 2 of 2

Malibu HS Draft Preliminary Schedule

Date	Revision	Checked	Approved
