

Start Date	02JUL07	MAST		Sheet 1 of 1	
Finish Date	11FEB17			Date	
Data Date	01AUG07			Revision	
Run Date	22AUG07 16:57			Checked	
				Approved	

**Santa Monica HS**  
**Draft Preliminary Schedule**

© Primavera Systems, Inc.





Orig Dur	Early Start	Early Finish	2007	2008	2009	2010	2011	2012	2013
			J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D J F M A M J J A	J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D J F M A M J J A	J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D J F M A M J J A	J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D J F M A M J J A	J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D J F M A M J J A	J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D J F M A M J J A	J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D J F M A M J J A

**Santa Monica HS Prog**  
**Measure BB**  
**Pkg #3(Bldg, Parking, Infrast**

Preconstruction	
<i>Bldg., Parking, Infrastructure &amp; Site</i>	
180 01JAN08	28JUN08
180 29JUN08	25DEC08
270 29JUN08	25MAR09
180 26MAR09	21SEP09
90 22SEP09	20DEC09


Construction	
<i>Synthetic Turf</i>	
270 21DEC09	16SEP10
270 01JUN11*	25FEB12

Demo & Construction: Bldg., & Park	
90 21DEC09	20MAR10
360 21DEC09	15DEC10
540 21MAR10	11SEP11
90 12SEP11	10DEC11
174 11DEC11	01JUN12


University Plaza	
77 15JUN10*	30AUG10
77 15JUN11*	30AUG11
77 15JUN12*	30AUG12

Utilities & Fire Life Safety	
984 21DEC09	30AUG12
984 21DEC09	30AUG12

Close-Out	
180 31AUG12	26FEB13

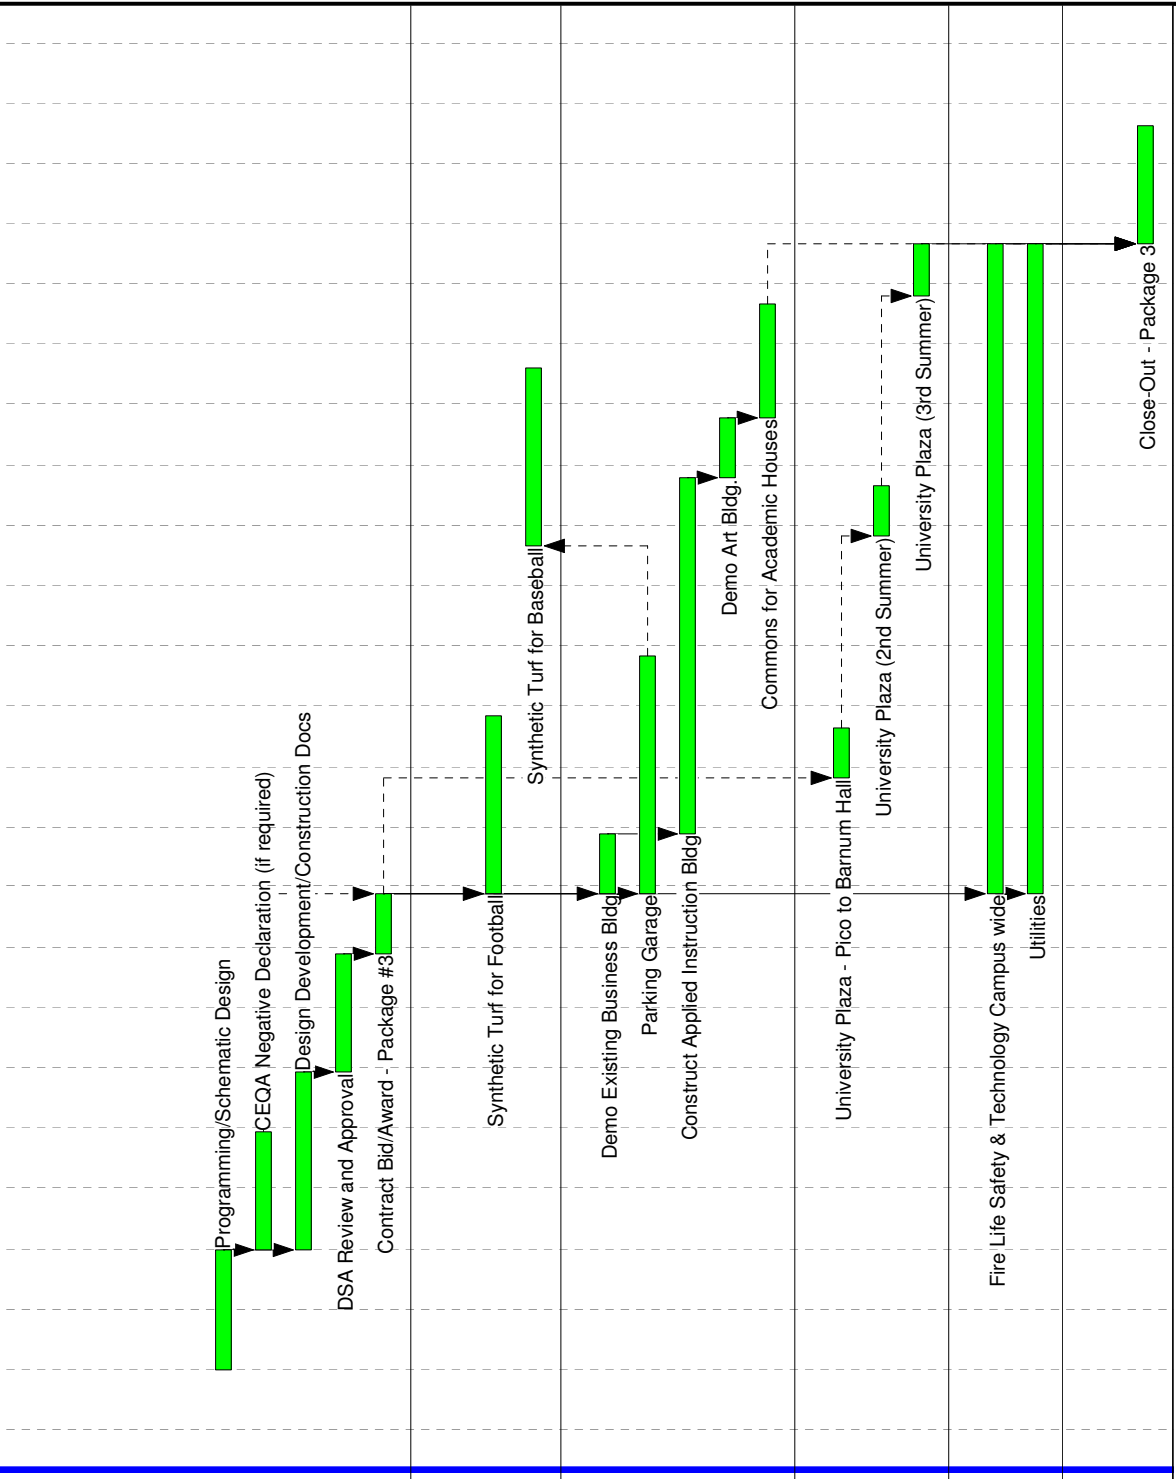

Start Date	02JUL07	Sheet 1 of 1	
Finish Date	11FEB17	MAST	
Data Date	01AUG07	<h2 style="text-align: center;">Santa Monica HS</h2> <h3 style="text-align: center;">Draft Preliminary Schedule</h3>	
Run Date	22AUG07 16:45		
Legend	<ul style="list-style-type: none"> <li><span style="color: green;">█</span> Early Bar</li> <li><span style="color: blue;">█</span> Progress Bar</li> <li><span style="color: red;">█</span> Critical Activity</li> </ul>	Date	Revision
		Checked	Approved

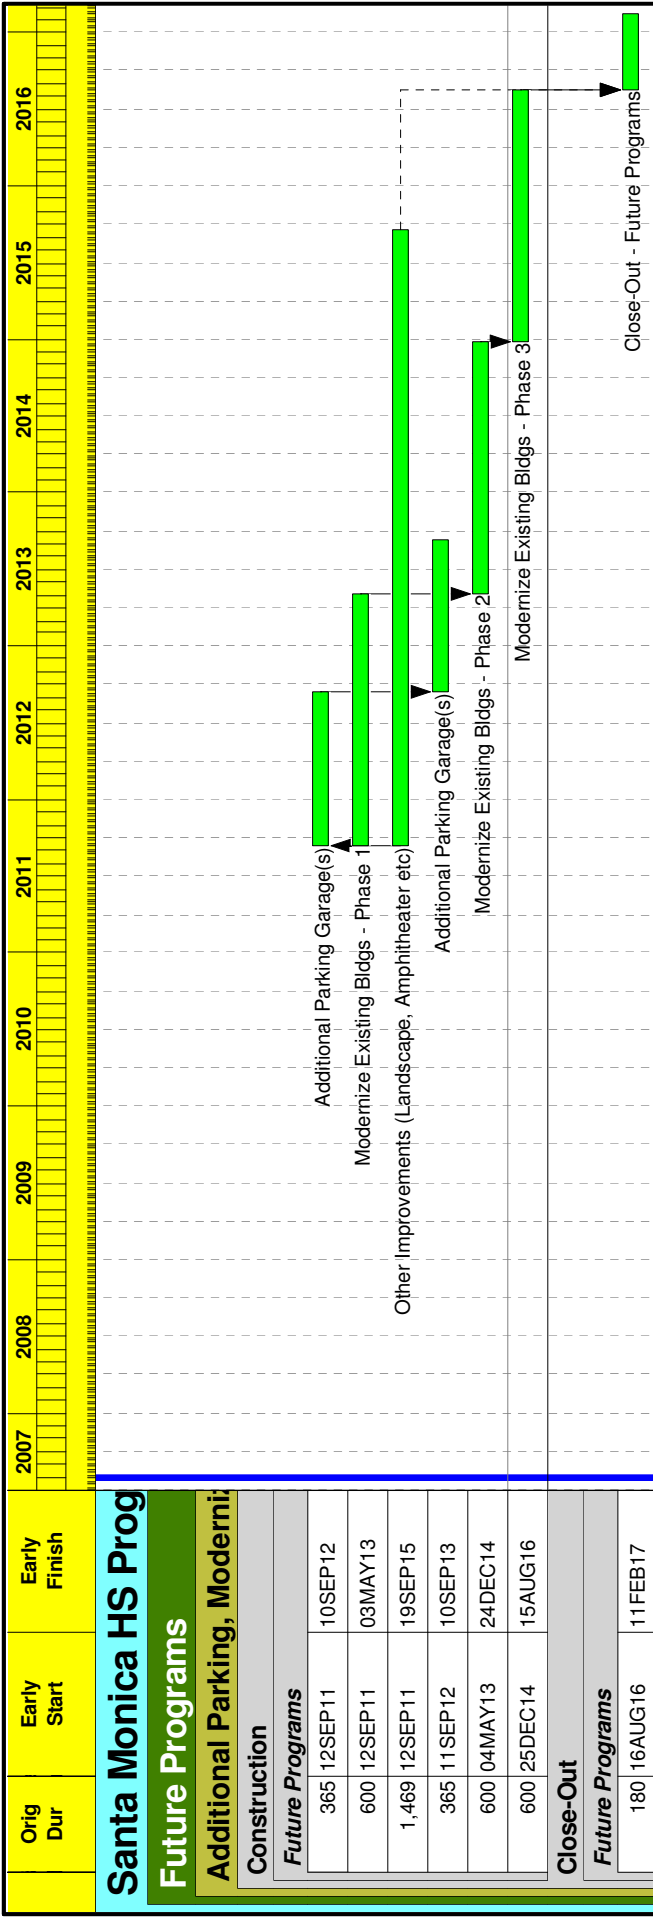

Sheet 1 of 1

MAST

**Santa Monica HS**  
**Draft Preliminary Schedule**


Start Date: 02JUL07  
 Finish Date: 11FEB17  
 Data Date: 01AUG07  
 Run Date: 22AUG07 16:46

Legend:  
 Early Bar: Green  
 Progress Bar: Blue  
 Critical Activity: Red

© Primavera Systems, Inc.

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Early Start	Early Finish	Budgeted Cost in Million	Year																			
						2008	2009	2010	2011	2012	2013	2014	2015	2016	2017	2018									
<b>Santa Monica HS Program</b>																									
<b>Measure BB</b>																									
<b>Pkg #1 (HVAC - Locker Room)</b>																									
<b>Preconstruction</b>																									
<b>HVAC Locker Rooms</b>																									
SMH1150	Design HVAC - Locker Room	180	01JAN08	28JUN08	0.00																				
SMH1170	DSA Review and Approval	120	29JUN08	26OCT08	0.00																				
SMH1175	CEQA Categorical Exemption	60	29JUN08	27AUG08	0.00																				
SMH1250	Contract Bid/Award - Package #1	60	27OCT08	25DEC08	0.00																				
<b>Construction</b>																									
<b>HVAC Locker Rooms</b>																									
SMH1130	HVAC - Locker rooms	180	26DEC08	23JUN09	0.00																				
<b>Close-Out</b>																									
<b>HVAC Locker Rooms</b>																									
SMH1260	Close-Out - Package #1	90	24JUN09	21SEP09	0.00																				
<b>Pkg #2 (Temp. Swing Space - Library &amp; Tech Shop)</b>																									
<b>Preconstruction</b>																									
<b>Temp. Swing Space - Library &amp; Tech Shop</b>																									
SMH2200	Design	180	01JAN08	28JUN08	1.45																				
SMH2230	DSA Review and Approval	120	29JUN08	26OCT08	0.48																				
SMH2240	CEQA Exemption	60	29JUN08	27AUG08	0.00																				
SMH4200	Contract Bid/Award - Package #2	90	25JAN09*	24APR09	0.10																				
<b>Construction</b>																									
<b>Temp. Swing Space - Library &amp; Tech Shop</b>																									
SMH5140	Swing Space in Existing Library & Tech Shop	120	25APR09	22AUG09	0.00																				
<b>Close-Out</b>																									
<b>Temp. Swing Space - Library &amp; Tech Shop</b>																									
SMH6340	Close-Out - Package #2	60	24AUG09	13NOV09	0.00																				
<b>Pkg #3 (Bldg, Parking, Infrastructure &amp; Sitework)</b>																									
<b>Preconstruction</b>																									
<b>Bldg., Parking, Infrastructure &amp; Sitework</b>																									
SMH1030	Programming/Schematic Design	180	01JAN08	28JUN08	1.45																				
SMH1040	CEQA Negative Declaration (if required)	180	29JUN08	25DEC08	0.00																				
SMH1060	Design Development/Construction Docs	270	29JUN08	25MAR09	4.24																				
SMH1070	DSA Review and Approval	180	26MAR09	21SEP09	0.48																				
SMH1080	Contract Bid/Award - Package #3	90	22SEP09	20DEC09	0.10																				
<b>Construction</b>																									
<b>Synthetic Turf</b>																									
SMH1220	Synthetic Turf for Football	270	21DEC09	16SEP10	0.00																				
SMH1230	Synthetic Turf for Baseball	270	01JUN11*	25FEB12	0.00																				
<b>Demo &amp; Construction: Bldg., &amp; Parking</b>																									
SMH1160	Demo Existing Business Bldg	90	21DEC09	20MAR10	0.00																				
SMH1180	Parking Garage	360	21DEC09	15DEC10	0.00																				
SMH1185	Construct Applied Instruction Bldg	540	21MAR10	11SEP11	0.00																				
SMH1205	Demo Art Bldg.	90	12SEP11	10DEC11	0.00																				
SMH1210	Commons for Academic Houses	174	11DEC11	01JUN12	0.00																				
<b>University Plaza</b>																									
SMH1190	University Plaza - Pico to Barnum Hall	77	15JUN10*	30AUG10	0.00																				
SMH1195	University Plaza (2nd Summer)	77	15JUN11*	30AUG11	0.00																				
SMH1200	University Plaza (3rd Summer)	77	15JUN12*	30AUG12	0.00																				
<b>Utilities &amp; Fire Life Safety</b>																									
SMH1270	Fire Life Safety & Technology Campus wide	984	21DEC09	30AUG12	0.00																				
SMH1330	Utilities	984	21DEC09	30AUG12	0.00																				
<b>Close-Out</b>																									
SMH6240	Close-Out - Package 3	180	31AUG12	26FEB13	0.00																				
<b>Future Programs</b>																									
<b>Additional Parking, Modernization &amp; Site Work</b>																									
<b>Construction</b>																									
<b>Future Programs</b>																									
SMH1280	Additional Parking Garage(s)	365	12SEP11	10SEP12	0.00																				

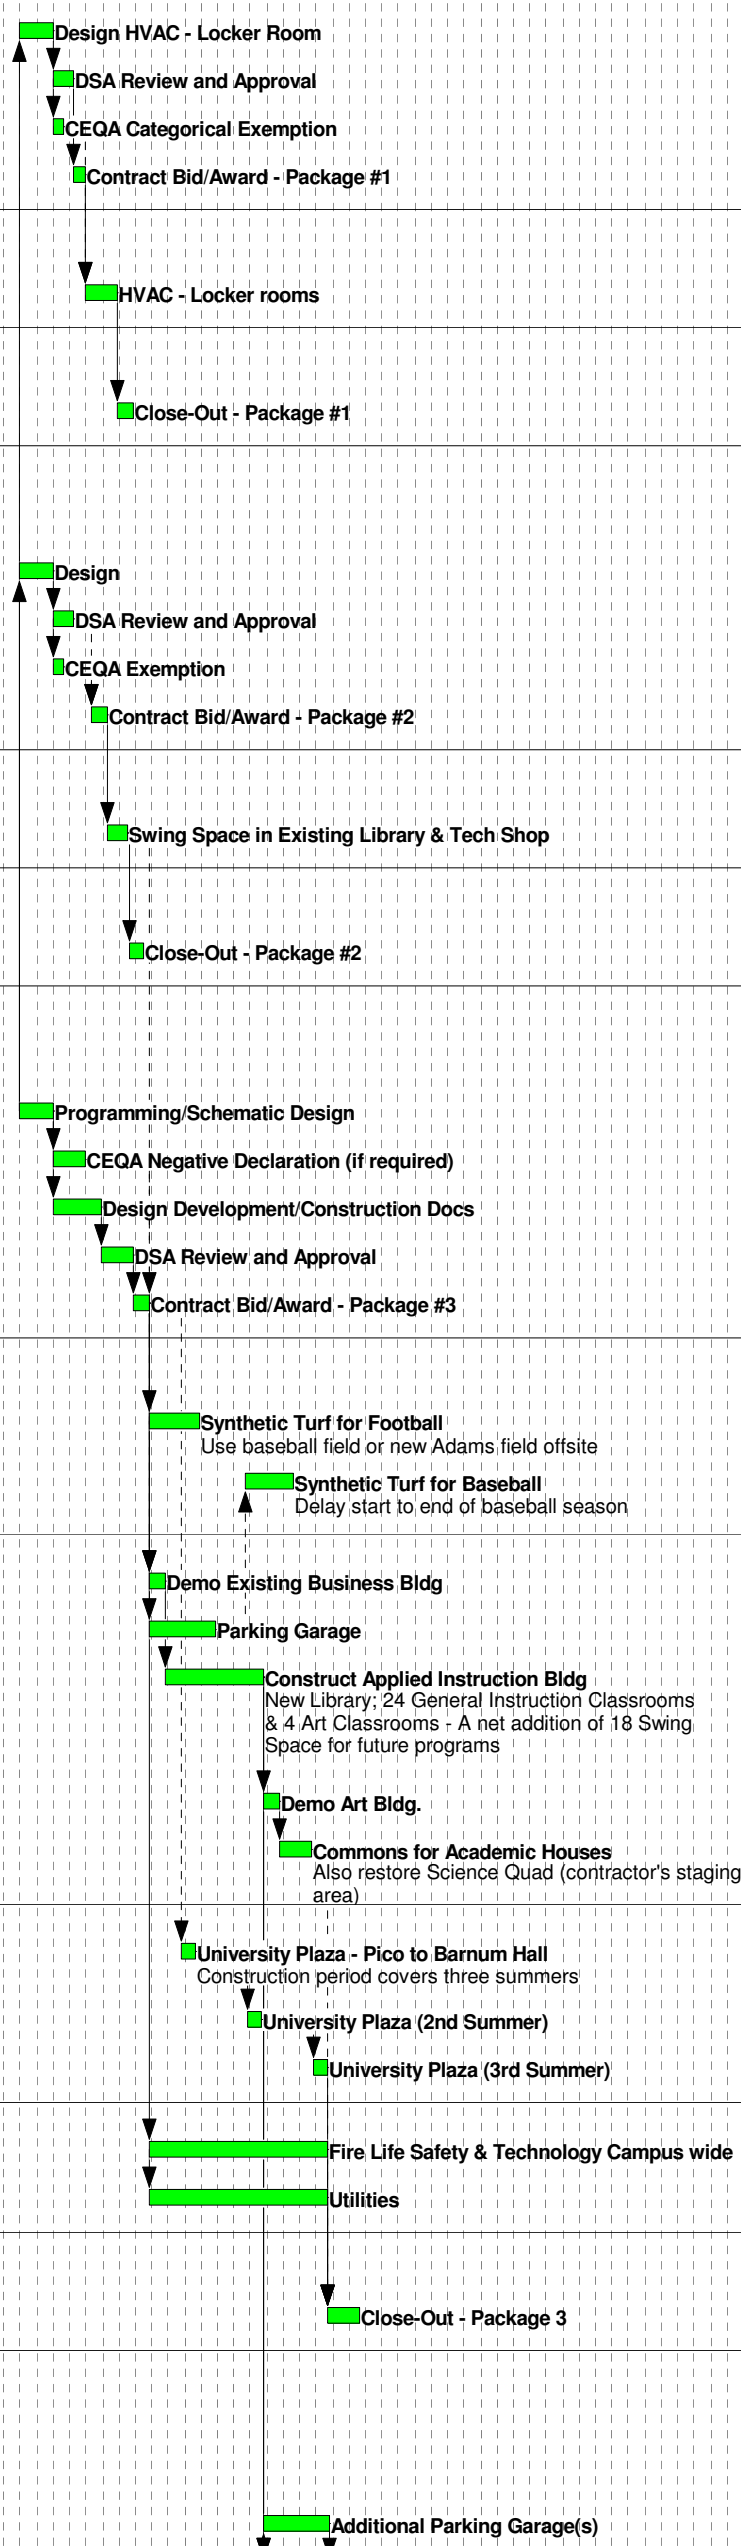

Activity ID	Activity Description	Orig Dur	Early Start	Early Finish	Budgeted Cost in Million	2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018											
						Gantt Chart Area											
SMH1300	Modernize Existing Bldgs - Phase 1	600	12SEP11	03MAY13	0.00	Modernize Existing Bldgs - Phase 1											
SMH1380	Other Improvements (Landscape, Amphitheater etc)	1,469	12SEP11	19SEP15	0.00	Other Improvements (Landscape, Amphitheater etc)											
SMH1290	Additional Parking Garage(s)	365	11SEP12	10SEP13	0.00	Additional Parking Garage(s)											
SMH1310	Modernize Existing Bldgs - Phase 2	600	04MAY13	24DEC14	0.00	Modernize Existing Bldgs - Phase 2											
SMH1320	Modernize Existing Bldgs - Phase 3	600	25DEC14	15AUG16	0.00	Modernize Existing Bldgs - Phase 3											
<b>Close-Out</b>																	
<b>Future Programs</b>																	
SMH1400	Close-Out - Future Programs	180	16AUG16	11FEB17	0.48	Close-Out - Future Programs											

Start Date 02JUL07  
 Finish Date 11FEB17  
 Data Date 01AUG07  
 Run Date 22AUG07 13:37

█ Early Bar  
█ Progress Bar  
█ Critical Activity

Date	Revision	Checked	Approved
